



ASSERT Project Plan

Overview of Project

1. Background

NaCTeM is the first publicly funded text mining centre in the world, supporting (with services and access to appropriate tools) the analysis of large collections of documents to discover previously unknown information. The establishment of NaCTeM has been as a result of an existing project currently funded by JISC (which has contributed £979,000) with additional funding from the BBSRC (Biotechnology and Biological Sciences Research Council) and the EPSRC (Engineering and Physical Sciences Research Council). The Centre is operated by the Universities of Manchester (lead partner) and Liverpool, with unfunded associate partners at the University of Geneva, the University of Tokyo, the University of California, Berkeley and the San Diego Supercomputer Centre and is currently focused on biosciences.

NaCTeM is one of the users of the National Grid that can demonstrate a direct relationship between Grid computing and the feasibility of its work, as many of the processes it undertakes would not be possible without Grid computing. NaCTeM's services are free of charge for usage by members of higher and further education institutions. Substantial institutional commitment to the establishment and on-going success of the text mining centre has been demonstrated by the partner universities, each of which have funded the secondment of at least the equivalent of one full-time member of staff to the project. Finally, the Centre is at a critical point as it has a global advantage in the text mining field and it is vital that it pushes into new areas to retain this lead for the UK.

The current project, **Automatic Summarisation for Systematic Reviews using Text Mining (ASSERT)** centres around providing for broader institutional involvement in text mining through a community call, while at the same time developing an exemplar service for the social sciences domain. An additional text mining expert for NaCTeM will participate in projects in the arts and humanities or other domains resulting from a community call. In parallel, the text mining expert will work with domain experts from within the social sciences. This background work developing an exemplar systematic review service will provide a foundation for the project work.

As a whole, ASSERT strongly contributes to the outcomes required by the e-Infrastructure programme:

- Greater participation by the social sciences in e-Research.
- Greater usage of the Grid for social science and arts and humanities based e-Research.

Currently there is very little use of text mining within the social science or arts and humanities areas. Despite this, there are potentially huge advantages to using text mining methods to save time for researchers, open up new areas of research and encourage new ways of doing research. There are also tangential benefits of demonstrating how the Grid can be used to help research with the social sciences and arts and humanities.

ASSERT thus interfaces with the social sciences community in two ways:

1. Development of a social sciences summarization exemplar service based on NaCTeM tools.
2. Support for the social science community projects involving text mining funded by the JISC as the result of a community call.

The community call has been proposed to further extend or adapt the functionality of the ASSERT tools for other social science based projects. Our intention is to show how different text types can benefit from text mining and provide demonstrable results in multiple areas of research. This will assist with further dissemination and will provide key case studies for the planned workshop.

2. Aims and Objectives

The overall aim of ASSERT is to encourage greater participation by the social sciences community in e-Research by developing text mining technology (summarisation service) to facilitate the production of systematic reviews and to support a number of community projects related with text mining applications.

Before undertaking any new policy, practice, research or before making any other decisions it can be useful to find out *what is already known* about an issue in a fair, unbiased manner, in order to be of any scientific value to the community. This knowledge may include the findings of individual research studies that might, alone, be limited in their applicability and vulnerable to bias. In order to minimise this bias, therefore, a large number of people and organizations, such as the Cochrane Collaboration (<http://www.cochrane.org>), the Centre for Reviews and Dissemination's guidelines (<http://www.york.ac.uk/inst/crd/report4.htm>) have developed methods for locating research evidence and synthesising it in order to inform decision-making. They have developed ways of conducting literature reviews of research in a systematic way, which provide users with a 'short-cut' to relevant evidence.

Systematic reviews usually proceed along the following stages:

(i) First, extensive *searches* are carried out in order to *locate* as much relevant research as possible according to a query. These searches often include electronic databases, scanning reference lists and searching for unpublished literature. This stage includes the definition of a set of inclusion and exclusion criteria on which the researchers base their searching.

(ii) Then the mass of data retrieved by this process is *screened* until only the most relevant and reliable literature remains to form the focus of the review.

(iii) Finally, the literature is *synthesised* and summary reports are written to inform policy and practice. The summaries of research that are produced in this *systematic* way are then used to help users of research to make evidence-informed decisions.

The overall objectives of the proposed exemplar service are:

1. to develop cost-effective and rapid methods for locating relevant studies for input to a systematic review using a combination of text mining techniques;
2. to apply a suite of text mining tools that will support novel methods of information management in the domain of social science systematic reviews (document clustering, information extraction and text summarization);
3. to demonstrate the applicability of the text mining technology in social sciences, in cooperation with the Evidence for Policy and Practice Information and Co-ordinating Centre (EPPI) currently heavily involved in producing systematic reviews;
4. to disseminate the benefits of text mining to the wider social sciences community via NaCTeM services.

We have identified a key partner to participate as service users and domain experts in the proposed service development. The EPPI is part of the Social Science Research Unit at the Institute of Education in London, and has been involved in research synthesis since 1993. It is part of the ESRC's National Centre for Research Methods (NCRM), focusing specifically on building upon existing approaches to research synthesis to build an integrating framework that accommodates diverse types of information and research.

The existing NaCTeM tools need to be minimally tailored in order to meet the requirements of the new project. This will involve the addition of some minor features and some tuning to make the tools more effective when applied to problems of systematic reviews and in the domain of social sciences. However, the bulk of the work will be to produce a tool for a **summarisation service**. Additionally, the summarisation tool must interoperate effectively with the existing NaCTeM tools. For this reason, we intend to make the new tool compliant to the NaCTeM software infrastructure, Unstructured Information Management Architecture (UIMA). UIMA is an open, industrial-strength, scalable and extensible platform that has been developed by IBM¹ since 2001. UIMA provides an interoperability layer which allows for the composition of multiple analysis tools into a single application. A recent

¹ Main contributions are from teams based at IBM Thomas J. Watson Research Center (New York), IBM Haifa Research Laboratory (Israel), IBM Development Laboratory Boeblingen (Germany) and IBM Almaden Research Center (California)

special edition of the IBM Systems Journal describes the framework in detail (<http://www.research.ibm.com/journal/sj43-3.html>)

The overall objectives of the proposed community call support are:

1. to liaise with domain experts from other institutions who will use text mining as an integral part of their projects supported under the community call
2. to configure appropriate text mining workflows for the specific purposes of the supported projects.

Currently, this task is performed mostly manually and encounters many problems. The proliferation of information in textual form means that the quantity of potentially relevant literature retrieved in the early stages of a review can become unmanageable. Reviewers have been accustomed to sacrificing specificity in their searches in order to ensure they have not missed any relevant studies. They conduct searches that yield large numbers of 'hits'. They then download the titles and abstracts, usually into bibliographic software, and look through them manually. This process is often called 'screening' and is the most time-consuming part of the review. Reviewers are finding that they sometimes need to scan through tens of thousands of titles and abstracts that are retrieved from large databases such as ERIC (<http://www.eric.ed.gov/>) and Medline (<http://www.nlm.nih.gov/>) to decide whether or not they meet the inclusion criteria for a review.

2.1 Progress to Date – 21st February 2007

During this period progress has been made in an investigation into requirements analysis for the system, both in terms of technical and user –focussed requirements. This is planned to continue over the next period and beyond as it develops towards specific areas in the evaluation framework and the creation of the gold standards for output. This has only strengthened the aims and objectives of the project and no changes have been made or are expected.

Our targets for the next period will therefore be according to the plan laid out. Specifically this will include:

- Further customisation of the document clustering tools and extension to prototype interface.
- Initial user evaluation of the early demonstrator with feedback gathering
- Ongoing dissemination of the project aims and objectives at NaCTeM, JISC and external events
- Initial work looking at the overlap between document clustering and named entity recognition as a start to further work on the information extraction tools.

2.2 Progress to Date – 25th May 2007

During this period there have been no changes to the overall aims of the project and progress has been steady. Our prototype tools are now fully working on real data sets provided by EPPI and have been customised to the domain and tasks at hand. Further work has been carried out to implement an associative search for finding documents that are similar to a given article. We are currently working on integrating this into the text mining workflow and providing a web interface to further publicise our work.

For dissemination activities we have been actively engaging the community with presentations and demonstrations at the E-Social Science showcase, the E-Science showcase and at all NaCTeM events with other researchers and industrial contacts. The local social science community have been approached to discuss potential areas of interest and activity as a preliminary to meeting with the wider community. Initial feedback has been excellent with a number of clear use cases defined to coincide with major challenges in social science research. As part of these activities we have gathered initial feedback and user evaluation from numerous sources which we intend to implement in the final version of the clustering software and provide as a web tool for wider evaluation purposes.

Initial work has been carried out with terminology analysis and named entity recognition to improve the interface. This is in advance of the work with information extraction but has significant overlap. Further work in this will continue over the next period.

The community call has been brought forward from 08/07 and was successfully delivered at the Capital Programme Briefing Day on the 9th May 2007. Initial communications have been positive with a deadline being set for submissions as 21 June 2007.

Our targets for the next period will continue according to the project plan, specific items include:

- Further development of the customised NER tool – D4.1 – Due 30/06/07
- Completion of the evaluation framework report – D2.2 – Due 31/07/07
- Definition of the gold standard results – D2.3 – Due 31/07/07
- Production of the prototype clustering web demonstrator – M1 – D3.2 – Due 31/07/07
- Support for the community call and review of submissions – T8.2 – Due 20 July 2007.

3. Overall Approach

3.1 Strategy

A number of phases can be identified in ASSERT required to make the summarisation services in social sciences a reality: (1) requirements analysis, (2) tool customisation (3) tool development (summarisation module) and (4) service exemplar development.

(1) The requirements analysis phase will involve close collaboration with the EPPI and will involve the following:

- Definition by the user of the criteria for the classification of systematic reviews. Systematic reviews are currently classified according to inclusion and exclusion criteria, which are elicited from systematic reviewers.
- Gathering of types of information required to produce a summary from social science related documents. In order to achieve this we will incorporate *viewpoints* (as defined by EPPI-Centre staff) to generate a summary, e.g. what is the background of a paper, methodology, outcomes, conclusions etc.

(2) The tool customisation phase will focus on the existing tools:

- T-MEMM part-of-speech tagger (bi-directional maximum entropy markov model)
- T-CFG parser (context free chunker)
- Enju deep syntactic parser
- TerMine terminology extraction system based on the C-value measure (hybrid system based on statistical knowledge and linguistic information)

For **parsing**, we will use our own deep linguistic HPSG parser, Enju (<http://www.tsujii.is.s.u-tokyo.ac.jp/enju/>). The efficient parsing algorithm of Enju and the wide-coverage probabilistic grammar it uses can effectively analyse the syntactico-semantic structure of complex sentences and provide us with the types of evidence needed in ASSERT. The annotated corpora will be kept as local copies and converted into XML to allow social science research groups to have indirect access via NaCTeM.

In order to proceed with the subsequent tasks, we assume that we have as a starting point a set of documents supplied by the user e.g. EPPI, which will then be clustered and summarised.

For **document clustering**, we will use the existing open source software CLUTO (<http://glaros.dtc.umn.edu/gkhome/cluto/cluto/overview>). CLUTO is a software package for clustering low- and high-dimensional datasets and for analyzing the characteristics of the various clusters. CLUTO is well-suited for clustering data sets arising in many diverse application areas including information retrieval, web, GIS, etc. CLUTO's distribution consists of both stand-alone programs and a library via which an application program can access directly the various clustering and analysis algorithms implemented in CLUTO. This software contains versions that run under Linux, UNIX and Windows environments. The goal of document clustering is to assign documents based on the topic they discuss. The produced clusters, also called **topic-clusters**, should ideally correspond to a topic that is shared by all the documents they contain and by no other document in the collection. Identifying the topic of a document is not a straightforward procedure. Current research in document clustering tends to use actual words and their frequencies that are contained within a document in order to identify the topic of a document. However the same word may be used to denote the same topic (polysemy, ambiguity) or different forms of the same word appear in text (variation). These occurrences may potentially divert the document clustering algorithm, leading it to incorrect decisions. Thus, any background knowledge (ontology) may enhance the clustering results attained by a

document clustering algorithm. If we can use ontologies to build links that correlate different terms appearing within the documents of our collection, then we can safely expect an increment in the quality of our clustering solution. However, in such domains the classification may be of more use especially if we have a good understanding of the different settings in which the objects participate.

Documentation of the software and a user manual can be found at <http://glaros.dtc.umn.edu/gkhome/cluto/cluto/download>.

We note that we will **leverage** from existing tools for document clustering since these are adequate for our purposes, allowing us to focus on the summarisation task.

(3) The core component of the project is the development of the summarisation module.

Summarisation takes as input the sentences extracted from our customised tools and is based on the identification of topics in the documents and the selection of salient sentences for each topic.

Next we will construct a classifier which will categorize the input information according to the viewpoints defined in step (1). For that purpose, machine learning techniques will be used on an annotated test corpus annotated (according to the **viewpoints** defined by the user). We will use a classifier based on Support Vector Machines (SVMs), which uses a number of features such as n-gram frequency, dependency relation, sentence position, etc. We will evaluate our classifier independently to determine its performance with respect to the specific task. The quality of the classifier is very important because it may affect the overall quality of the summarization system. The output of this step is a set of automatically extracted sentences that include the viewpoints as discovered by the classifier.

The last step produces the summary. It takes as input the sentences extracted in step 3. These sentences now contain an annotation of the viewpoints which make up the summary. We adopt the following strategy to summarize information:

- we divide the document to be summarized into sub-sections according to the viewpoints given by the user (sectioning);
- we extract the most salient description from each viewpoint, and
- we exclude redundant information scattered over the input documents.

An important aspect of this sectioning step is the statistical analysis (e.g. term frequency, sentence location, clue phrases, etc.) of the input documents and the extracted sentences. Examples of sectioning are: **background, conclusions, methodology** etc. Sectioning will be based on the viewpoints provided by the EPPI reviewers.

We adopt a practical solution to summarization as it is still very difficult to generate comprehensible summaries from an internal linguistic representation. In addition, domain specific documents use a number of technical terms (and variants) for describing the same concept. Hence, it is crucial to carefully perform the statistical analysis to improve the quality of a summary, incorporating terminological variations such as synonyms, acronyms, etc. Our summarization system is based on a systematic terminological analysis which is important for domain specific areas.

All terms in the documents are mapped into concepts using thesauri such as the HASSET Thesaurus <http://www.data-archive.ac.uk/search/hassetSearch.asp>, the National Public Health Thesaurus and the British Education Thesaurus. We will use as features concept- concept pairs by examining co-occurrences within sentences. The weights of concept-concept relations are calculated by using the frequency of the co-occurrences.

To detect a set of topics in the source documents, we shall apply EM clustering to the source sentences represented by the features (i.e., concept-concept pairs). Unlike the k-means clustering, EM clustering does not assume each cluster to have the same number of instances (sentences), which is a good characteristic for the topic detection.

(4) This phase will focus on the development of a service exemplar. This exemplar will serve a number of purposes. Firstly, it will address real problems encountered by the social sciences community. Secondly, it will demonstrate the effectiveness of the tools developed by the Centre as a means of solving problems. The initial focus of this activity will be to link the exemplar with the identified requirements of the social sciences community (EPPI). This will have the added benefit of ensuring a close interaction and cooperation with EPPI throughout the project.

The distribution of work between NaCTeM and EPPI is shown below; B, D, E, G (NaCTeM), A,C,F,H (EPPI)

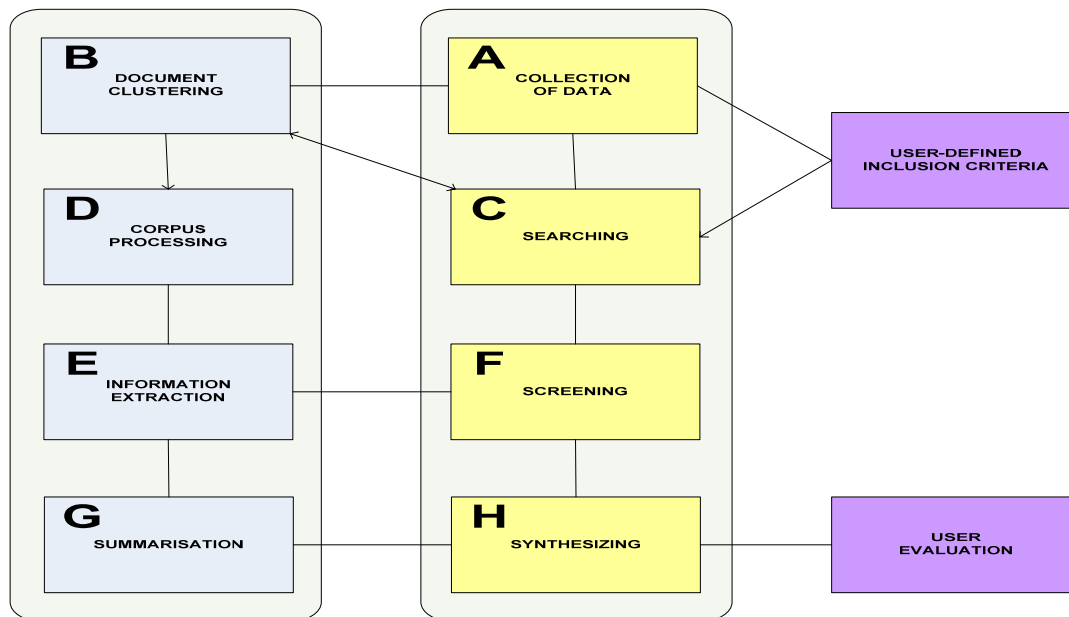


Figure 1: Architecture of the project and distribution of the work

3.2 Important Issues

External users will be able to access to the Centre's text mining tools integrated with the software infrastructure at the end of the second year of ASSERT.

At the earliest feasible stage, we will expose our summarisation system to EPPI community, expanding to the wider social sciences community once our tool has been demonstrated to exhibit the following characteristics:

- robustness
- efficiency
- scalability

Scalable, robust, efficient and rapidly responsive services for very large collections, simultaneous requests, the need to consult large-scale resources (corpora and thesauri) are critical aspects of the service provision.

- Focus on *user-need* related development whilst using experts to feed-in research results. Early involvement of the EPPI users will ensure this characteristic.
- Documentation and awareness are also crucial aspects of the user experience and will be core activities during the development work.

3.3 Scope and boundaries of the work

Text mining technologies have the potential to revolutionize the way we approach research synthesis. Using automated techniques rather than people to perform this time consuming task, reviews would be completed much more quickly and would therefore be much cheaper. They would also be timelier – and become a more useful mechanism for informing decisions which need to be taken relatively quickly. Moreover, if text mining technologies carry out this task, then the development of complex electronic search strategies which combine sensitivity with the retrieval of a manageable number of

references would be less critical. Search strategies could simply be as sensitive as possible – with computers managing the screening of hundreds of thousands of potentially relevant references.

Our work in ASSERT will be application-oriented and will concentrate on the following:

- customising existing tools and
- developing a new text mining component (summarisation module).
- providing scalable text mining software

Wherever possible we will take advantage of existing work by the Grid and cluster computing communities. The close involvement of Manchester Computing, one of the partners in the JISC-supported National Grid Service, and the wider e-science community will be invaluable in this respect.

The aims of ASSERT are to produce a summarisation and sectioning tool for systematic reviews. We will not enhance or customise the document clustering algorithms for our purpose.

3.4 Critical success factors.

ASSERT will have a strong **user focus**; we will be developing a text mining service for the social sciences community. We have identified a specific problem within systematic reviews and we will address this problem.

Our evaluation will be performed from two aspects:

- evaluation of the text mining components; performance of the summarisation component
- user oriented evaluation: feedback from EPPI whether text mining technology actually facilitates the task of searching and screening in systematic reviews.

Critical success factors in the success of the project will include:

- **Positive user responses** to our services. It is important that we conduct an ongoing dialog with our user communities.
- **Scalability** of the tools that we provide. The capabilities of text mining have not been yet explored in social sciences, and ASSERT will be the first to do so. Existing tools like qualitative based analysis (QALDAS) content analysis do not deploy text mining techniques. ASSERT will enhance the capability of existing tools used in social sciences.
- The ease with which the software infrastructure allows other tools to **interoperate** will be another important factor in our success. We believe that adoption of the tools and infrastructure provided by the Centre will be greatly increased if other developers are able to straightforwardly integrate their own tools with ours. This integration must therefore be based on the cooperation of loosely-coupled systems, avoiding any requirement for major rewriting of existing software. **Interoperability** is the ability to combine modules and exchange data, meta-data and other resources to maximise their re-use <http://www.ukoln.ac.uk/interop-focus/about/leaflet.html>. There are several ways to achieve interoperability:
 - Modules can communicate through remote procedure calls
 - Web Services
 - common APIs
 - common data exchange formats. In this case, every module has to comply with the output format of the previous components,
- **Open standards** are a vital mechanism in achieving interoperability and acceptance amongst the wider community. We will adopt existing standards where they are available.

3.5 Progress to Date – 21st February 2007

There have been no changes to the overall approach involved, however after further requirements analysis a number of changes have been made to the choice of software planned for use. Instead of using Enju, a shallow parser will suffice to obtain similar results in a more scalable manner, ideal for the very large document collections used in the systematic review process. It has also been decided to investigate further the choice of information retrieval engine. The choice is currently between the Cheshire system and Lucene, both with significant benefits and limitations. An internal report on this

will be made available in the next period, with a decision and justification of the choice. Further information on both of these issues is available in section 9.1.

3.6 Progress to Date – 25th May 2007

It has been decided that Lucene will be used for all further information retrieval tasks in this project. The main reasons for this choice are documentation, uptake of software and ease of integration into JISC and related infrastructure. No further changes have been made to the overall approach detailed in the project plan.

4. Project Outputs

The output would be a service that would automatically collect information about specific topics (as specified by the user), consult with knowledge bases using a combination of text mining techniques to augment the search topics, and automatically provide relevant summaries. This service would assist systematic reviewers in the social sciences in classifying and summarizing the thousands of abstracts and full texts of primary research studies according to the reviewers' viewpoints. It would be backed up by an exemplar based on the practices and documents used by the EPPI-Centre, since this is a good application of the usefulness and applicability of text mining tools and techniques in systematic reviewing. The exemplar would summarize an article or a set of articles by matching the relevance of documents to the user defined criteria by:

- Clustering documents relevant to the user's information need by improving searching using a combination of text mining techniques and existing knowledge sources (thesauri);
- Identifying and classifying the relevant types of information using information extraction;
- Generating summaries by "condensing" the classified information.

The main outputs of this project are therefore:

- A summarisation service (D5.3)
- An exemplar tool for EPPI systematic reviews (D6.2)
- Documentation about how to use the tools and the service
- Training support for both sets of software

In addition to this the community call and its developments will have their own outputs which will be detailed further upon successful applications

Appendix B documents the project schedule and deliverables in more detail.

4.1 Progress to Date – 21st February 2007

Excellent progress has been made in this first period. Three early deliverables are already available:

- D2.1 – Two sets of test data have been made available by EPPI
 - Mental Health
 - Walking and Cycling
- D3.1 – The customisation of the clustering tools is going well, leading to an early demonstrator of the tools, designed to elicit feedback from users during the requirements analysis phase.
- D7.1 – A web site has been constructed for the project. It is available at <http://www.nactem.ac.uk/assert> and will be updated as the project continues.

All planned deliverables for this period have been submitted on time and the first milestone for the project is currently ahead of schedule.

4.2 Progress to Date – 25th May 2007

Good progress has been made in this period with sustained development of software running smoothly, alongside key dissemination and requirements gathering activities. The main output for this period has been the successful development and testing of the customised clustering tools on EPPI data (D3.1). This has run alongside work on the evaluation framework (T2.2) and investigations into a gold standard (T2.3). The full outcomes of these activities are expected in the next period.

All planned deliverables for this period have been prepared on time and the first milestone for this project is marginally ahead of schedule.

5. Project Outcomes

We envisage the major intangible outcome of the project will be a general raising of awareness of text mining in the social sciences community, and of the tools that are available. NaCTeM has recently organised a dedicated workshop on “Bridging qualitative and quantitative research methods for social sciences using text mining” funded by the ESRC National Centre for e-Social Science <http://www.ncess.ac.uk/events/agenda/textmining/>

Through direct involvement in the community projects (the e-Research framework) we will identify requirements for the following text mining applications such as:

- sentiment analysis
- content based analysis
- qualitative analysis tools
- forensic linguistics
- authorship identification
- etc.

NaCTeM is already acting, via the organization of workshops, tutorials etc as an **educator** in text mining technology to biosciences.

The new project will allow us to enhance the take-up of text mining in the social sciences.

Potential beneficiaries and users of the project outputs will include researchers in:

- qualitative inductive research
- social sciences
- e-social science

A dedicated workshop related with the issues, problems and solutions for systematic research synthesis and a demonstrator of the text mining tools deployed for that purpose, will be organized in conjunction with the users (EPPI) and the National Centre for e-Social Science.

5.1 Progress to Date – 21st February 2007

As one of the key outcomes of this project is raising the awareness of text mining activities in the social sciences we have been actively pursuing high visibility external collaborations. We are pleased to announce that one such confirmed collaboration will be with the BBC using some of the outputs from the document clustering tools upon news articles. This pilot study and associated dissemination activities will bring the core demonstrable tools out of the biomedicine domain into a more readily acceptable and understandable general domain. With enthusiastic partners we hope that this pilot will extend out to more collaborations leading towards possible exit strategies and more importantly improved sustainability. Current schedules for this project make the deliverables due during the community call phase of the ASSERT project allowing us to leverage them for demonstrators to encourage engagement.

5.2 Progress to Date – 25th May 2007

The project has made good progress in raising the awareness of the benefits of text mining tools for social science research within the community around the area of Manchester. This is a preliminary stage to discover further use cases before expanding the dissemination activities to the wider UK community. Our dissemination plan draws upon the experiences discovered at previous JISC and AHRC events that for maximum impact and future uptake we should take our demonstrations to social science events, not only invite those interested parties to come to us. Given the knowledge of the key challenges and issues in the social sciences it will become much easier to engage with the audience using clear and concise examples from known problems.

Dissemination

Sophia Ananiadou presented ASSERT as part of NaCTeM's activities during the ESNW awareness day which took place in Manchester on the 2nd May 2007.

As part of our future dissemination we are co-organising with NCeSS and ESNW a text mining awareness day within the framework of e-Science on Text Mining for the e-researcher. Relevant aspects on text mining for the social sciences will be discussed during the panel discussion.

Publications

Paper authored by Brian Rea and Sophia Ananiadou was submitted and accepted for publication to the All Hands Meeting Conference, September 2007.

Paper authored by Sophia Ananiadou, Brian Rea, James Thomas and Rob Procter was submitted to the 3rd International Conference for e-Social Science.

6. Stakeholder Analysis

Stakeholder	Interest / stake	Importance
NaCTeM	<p>NaCTeM will customise text mining tools for the UK social sciences community and in particular EPPI.</p> <p>NaCTeM will consolidate text mining as a scientific activity in its own right, by demonstrating its applicability in a variety of domains and text types.</p> <p>NaCTeM will ensure service provision in social sciences</p> <p>NaCTeM will revolutionise the way systematic reviews are conducted.</p>	High
University of Manchester	<p>Enhancing the image and visibility of the University as leading text mining for the social sciences community</p> <p>Making the University a focus of excellence in text mining</p> <p>Investment in NaCTeM and text mining research</p>	High
HEFCE (JISC)	<p>Allocation of significant resources to the Centre with expectation of development of service that is relevant to the needs of the social sciences community.</p> <p>Strategic alignment through capital programs</p> <p>Expanding into e-Research, e-Social Science programmes</p>	High
EPPI	<p>Improving the way they conduct systematic reviews</p> <p>Allocation of resources to annotate a gold standard</p> <p>Provision of requirements analysis</p> <p>Evaluation of text mining tools for their needs</p>	High
National Centre for e-Social Science, e-Research, ESRC	NaCTeM will engage in complementary activities,	High

	leading to synergistic and cross-group activities to develop new insights and further both individual aims and UK-wide collective success.	
E-Infrastructure	Alignment with other programs Community engagement Alignment with National Grid services	High
Academic users in social sciences	NaCTeM will provide services and support to the wider social sciences community	Medium
Respondents to the community call	Support from text mining services Engagement with NaCTeM Seeking catalysis of a text mining community in social sciences in the UK	High

6.1 Progress to Date – 21st February 2007

A key focus on user needs and expectations has led to ongoing consultation with our partners in EPPI and other potential user communities. We hope to extend this further now that an example demonstrator prototype is available as this will boost engagement with potential future users. Locally, we are leveraging the experience, expertise and contacts of NaCTeM and the University of Manchester to ensure state of the art technologies are used and high visibility to commercial contacts and potential future stakeholders. With the project now fully defined and on target we hope to extend our communications further in the next period towards HEFCE and the wider UK academic community in preparation for the community call. This will enable wider communication and visibility with the programme and enable improvements to the project based on the experiences of others involved in similar undertakings.

6.2 Progress to Date – 25th May 2007

During this period we have continued development of the evaluation strategy based upon discussions with James Thomas and NCeSS. These methods will include regular user testing with members of the EPPI reviewing team and in the latter stages parallel investigations using manual methods compared with technology assisted approaches. We believe that this key testing in the end-user environment within existing manual workflows, will be crucial in evaluation the software and in the assessment of the results of key project objectives.

Academic users in the social sciences have been approached on a number of occasions during this period to demonstrate current progress and discuss the benefits of using text mining technology. Support has been better than expected with many potential areas for extension being highlighted. Key to this is that some of the major challenges facing social scientists have been discovered allowing further informed discussion with the wider social science audiences over the coming months.

7. Risk Analysis

Risk	Probability (1-5)	Severity (1-5)	Score (P x S)	Action to Prevent/Manage Risk
Staffing				
Unable to recruit staff in specialised area	3	5	15	Re-advertise the post Existing staff can cover initial tasks if necessary; expertise and know-how in house
Staff retention may be difficult	2	4	8	Expertise existing in NaCTeM to cover for a short period; re-advertise
Organisational				
Not engaging with the community call stakeholders	2	4	8	Ensure early involvement of NaCTeM in the formulation of the community call --Identify and target users in social sciences who would benefit from use of TM technology --Participate in the call.
Lack of support from the University	1	4	4	Continue to maintain interest in text mining from UoM management as an important interdisciplinary area Engage with UoM social science academics via open days and workshops
Technical				
Lack of required technical expertise	1	5	5	Skills audit to identify any gaps in knowledge. Identify training requirements and arrange training.
Delivery of summarisation hampered due to support of community call	4	5	20	Constrain the amount of support to the community call within reasonable limits Distinguish specialised and general support of text mining; offload general support to NaCTeM helpdesk
Open source tools lose support	3	1	3	Use alternative tools of similar functionality
Not producing summaries according to the criteria of readability, lack of redundancy, production time	2	5	10	Ensure that recruitment of technical staff can deliver appropriate software Techniques well defined and measurable Early involvement and constant evaluation from EPPI users

Legal				
License infringement	1	3	3	Different tools have different licences Care needs to be taken about how the tools are combined.
IPR of tools become restricted	2	2	4	We are based on our own NaCTeM tools to develop the summarisation tool Open licence agreement
Sustainability				
Low take up of tools and services	2	5	10	Extensive requirements gathering. Make services widely available via NaCTeM / Mimas. Dissemination activities via seminars and tutorials.

8. Standards

Name of standard or specification	Version	Notes
UIMA		Infrastructure for text mining pipeline
W3C web service standards		Maintaining web services
XML		Mark-up language
DocBook		XML-based structural-level mark-up language.

8.1 Progress to Date – 21st February 2007

There have been no changes to the standards involved in this project. Where appropriate they are being fully implemented. UIMA compliance will only be built into the final version prototypes as laid out in the project plan.

8.2 Progress to Date – 25th May 2007

With the development shifting to the Java programming language of Lucene, it is possible to add other standards to the projects. We have investigated the use of web service standards as part of the work in linking the software into existing text mining work flows but this has shown that the data intensive nature of this work makes this unsuitable. We are continuing to identify new standards as they become accepted and update our tools when changes are made, as appropriate.

9. Technical Development

Technical development will adhere to the general provisions of the NaCTeM service development process documented in the NaCTeM project plan. This includes the setting up of proposed solutions and use cases, system architecture and service roadmap. We will exploit the NaCTeM Subversion source code control repository and policy to ensure that service development follows best practice. This covers source control, source code standards, daily builds, automated tests and versioning.

9.1 Progress to Date – 21st February 2007

Technical development is continuing along the guidelines laid out by NaCTeM and is on schedule with the plan. An internal progress report, available on the ASSERT website at <http://www.nactem.ac.uk/assert/reports/internalReport130207.pdf>, details progression and many of the issues involved. In summary the Information Extraction work package has changed to accommodate issues during the requirements analysis phase. To improve efficiency we will not be using Enju as a full parsing system, but will use a shallow parsing system instead. This will provide us with all of the information we require for this project without additional processing of, what would become, unused information. In light of this we have introduced a named entity recognition package to assist in semantic evaluation of the terminology. These technical changes do not affect the overall approach and will go unnoticed by the user.

9.2 Progress to Date – 25th May 2007

Technical development is continuing along the guidelines laid out by NaCTeM and is on schedule with the plan. The proposed change of information retrieval software has now taken place. Lucene is in active use with datasets provided by EPPI. We have added associative searching as requested by users and in line with other providers.

10. Intellectual Property Rights

The summarisation software will be released under a licence agreement in accordance with the JISC policy and the existing tools of the National centre. The released software will be available in perpetuity. Copyright University of Manchester.

- Enju: copyright held by University of Tokyo
- T-MEMM part-of-speech tagger (bi-directional maximum entropy markov model) : copyright held by University of Tokyo

- T-CFG parser (context free chunker) copyright held by University of Tokyo (all available through NaCTeM and covered by NaCTeM consortium agreement and licensing)
- TerMine: copyright held by University of Manchester
- CLUTO open source software copyright University of Minnesota

10.1 Progress to Date – 21st February 2007

All third-party rights were agreed before work began on the project, there have been no modifications to this. The substitutions in software (highlighted in section 9.1) for the components NER and chunking software will be using tools internal to NaCTeM. Cluto is available for download and will be open-source in the future and may be freely used for educational and research purposes by non-profit institutions.

10.2 Progress to Date 25th May 2007

Lucene is available under the Apache software licence giving permission to distribute and use the software for any purpose as long as notifications and disclaimers from the original software are included. No additional IPR issues have been raised with us during this period.

Project Resources

11. Project Partners

University of Manchester

Main contact: Dr Sophia Ananiadou
 School of Informatics
 University of Manchester
 Manchester
 M60 1QD

e-mail: Sophia.Ananiadou@manchester.ac.uk

Phone: (0161) 306 3092

Role: Leading the project. 1 full-time research associate, fully-funded by JISC.

EPPI

Main contact: Dr James Thomas

Social Science Research Unit
 Institute of Education, University of London
 18 Woburn Square
 London
 WC1H 0NR

telephone: +44 (0)20 7612 6844

fax: +44 (0)20 7612 6400

email: j.thomas@ioe.ac.uk

Role: problem provider, requirements, evaluation, no funding from JISC

11.1 Progress to Date – 21st February 2007

There have been no changes in the project partnership.

11.2 Progress to Date – 25th May 2007

There have been no changes in the project partnership.

12. Project Management

The project manager for this project will be Dr Sophia Ananiadou, School of Computer Science, University of Manchester. The work will be managed in line with the JISC project management guidelines.

13. Programme Support

Consultation regarding the related upcoming community call.

13.1 Progress to Date – 21st February 2007

There are currently no specific areas where we would like support from the programme.

13.2 Progress to Date – 25th May 2007

During the review stages of the community call we anticipate a need for support from the programme to assist in evaluation of submissions, alongside a review panel, to ensure suitability for funding.

14. Budget

Detailed budget for the proposal, profiled over Academic Year

	2005/06 AY	2006/07 AY	2007/08 AY	Total
Staff salary ²	£3,107	£38,773	£36,964	£78,844
Overhead	£4,472	£53,894	£49,618	£107,984
Contribution from University of Manchester ³	-£3,014	-£36,394	-£33,576	-£72,984
Dissemination	£1,800	£6,800	£6,800	£15,400
Equipment	£8,856			£8,856
Community call		£161,000	£200,900	£361,900
Total	£15,221	£224,073	£260,706	£500,000

14.1 Progress to Date – 21st February 2007

December 2006 to February 2007

Staff Costs	£ 10,454.84
Equipment	£ 1,180.00
Dissemination	£ 87.40
Total	£ 11,722.24
Overheads 44%	£ 5,157.79
Grand Total	£16,880.026

Costs occurred during this period are as according to plans.

14.2 Progress to Date – 25th May 2007

March to May 2007

Staff Costs	£ 6,264.70
May salary costs	£ 3,129.42
Total	£ 9,394.12
Overheads 44%	£ 4,133.41
Grand Total	£ 13,527.53

Costs occurred are as according to plans. There will be a significant spend on equipment during the next phase to ensure suitable infrastructure for planned services.

² Assumes pay award of 4% per annum and includes overheads.

³ There is a strong level of commitment from Manchester University to recruit an additional text mining expert as they feel that this resource is vital to the continued growth of NaCTeM. They are therefore prepared to make a significant contribution to the overheads for this person.

Detailed Project Planning

15. Work-packages

Work-package	Summary
1 Project Management	Managing the day-to-day activities of the project. Ensuring that deliverables are delivered on schedule. Writing plans, progress reports and completion report.
2 Requirements Gathering and Evaluation	Test data gathering, requirements analysis by users, set up of evaluation methodology, creation of gold standard. Ongoing third party evaluation throughout project and testing.
3 Document Clustering	Use of document clustering software and integration into the NaCTeM pipeline
4 Information Extraction	Customisation of existing text mining tools for social science applications
5 Summarisation	Development of a scalable summarisation engine; integration into existing NaCTeM software infrastructure
6 Service Exemplar	Development of service exemplar which demonstrates the full capabilities of the summarisation tool.
7 Dissemination	Development of a Roadmap for availability of summarisation service, presenting work to conferences, organisation of a workshop, project web site
8 Support for the Community Call	Promote text mining through dissemination activities and engagement with user groups

15.1 Progress to Date – 21st February 2007

Substantial progress has been made against the plan resulting in a prototype demonstrator of the document clustering system being available early and assisting in the requirements analysis phase. All deliverables in this period have been completed on schedule. Further information on specifics of activity can be found in the internal progress report dated 13/02/07, available from the ASSERT website. A decision has been made to swap the order in which work packages 3 and 4 will be carried out. This has been due to results of the requirements analysis phase suggesting changes to the technical plan. A new task has been added to investigate the use of Named Entity Recognition software to assist in document clustering and as a preliminary to the information extraction work. We have included several new tasks and deliverables (T/D 3.1 & 4.1) to improve communication with partners and to ensure thorough and regular user evaluation and expectation reviews to be completed. Finally we have added T/D 6.2 to incorporate any feedback from the final evaluation phase back into the service exemplar before the end of the project.

15.2 Progress to Date – 25th May 2007

There have been no changes to the overall set of tasks and deliverables in this period. Work has progressed well according to the schedule laid out in the plan. With completion of the customised clustering tool (D3.1) and active dissemination and demonstrations (WP7) we have forged a very positive start for the project. This has run closely alongside further requirements gathering and evaluation with key stakeholders (T2.1 and T2.2). We have successfully prepared and presented the community call (D8.1) and are gathering appropriate reviewers to mark the submissions. Further work has been carried out adapting the NER software for this project (T4.1) and initial integration into a workflow for the purposes of advancing the clustering demonstrator (T3.2) in preparation for Milestone deliverable in the next period (M1).

Our objectives for the next period will continue according to the project plan, specific items include:

- Further development of the customised NER tool – D4.1 – Due 30/06/07
- Completion of the evaluation framework report – D2.2 – Due 31/07/07
- Definition of the gold standard results – D2.3 – Due 31/07/07
- Production of the prototype clustering web demonstrator – M1 – D3.2 – Due 31/07/07
- Support for the community call and review of submissions – T8.2 – Due 20 July 2007

16. Evaluation Plan

Evaluation is an essential part of a practical discipline like automatic summarization. In general, evaluation of automatic summarization is categorized into two types: intrinsic evaluation which tests the system in itself; extrinsic evaluation which tests the system in relation to some other task.

Two kinds of intrinsic evaluation are typically carried out using summarization.

- The first is a quality evaluation which measures how a summary reads. This can be assessed by on-line evaluation (e.g., having subjects grade summaries for readability) or off-line evaluation (e.g., metric to measure readability).
- The second type of intrinsic evaluation is the degree of informativeness, which measures how much information from the source a summary preserves at different levels of compression. This can also be assessed by on-line or off-line evaluation similarly to the quality evaluation.

The idea of an extrinsic evaluation is to determine the effect of summarization on some other task. A variety of different tasks have been proposed, for example, finding documents relevant to one’s need by reading summaries, effort required to post-edit a summary to bring it to some acceptable state, etc.

In order to conduct proper evaluation, the creation of a gold standard would be required. This task can only be conducted by the EPPI. In case, due to lack of resources, we are not able to have access to a gold standard other evaluation strategies will be investigated and adopted. These may include comparison of a generated summary with an existing systematic review to determine readability, lack of redundancy, informativeness, production time, etc

Timing	Factor to Evaluate	Questions to Address	Method(s)	Measure of Success
Tool Evaluation (Summarisation System)				
Month 14	Readability, content of system output according to requirements	Is the system useful to support systematic reviewers?	Evaluation metrics for summarisation and feedback from users	Performance rates according to existing metrics and response from users (70% rate system as useful)
Month 20	Scalability, speed	Is the speed of the system adequate for large scale use?	Metrics	75% of users rate system as useful for daily use
Dissemination				
Month 22	Awareness of usefulness of text mining for social sciences	Is the social scientist aware of the usefulness of text mining?	Evaluation questionnaire after workshop	70% of respondents award satisfactory score or better

16.1 Progress to Date – 21st February 2007

Though the main bulk of the planned evaluation takes place towards the end of the project, there has been an ongoing effort to ensure formative evaluation takes place both on a technical and user focussed level from the early stages of development. All software for this project regularly goes through detailed systematic testing according to the guidelines laid out by NaCTeM for best practice. When possible this is also put through user evaluation to test the interface usability, validity of the results and applicability to user functionality. The next planned stage of user evaluation on the

document clustering prototype is planned for March and the results of this will be made available as an internal document. As the document clustering demonstrator develops more fully this will continue to ensure the end result is not only accurate, but is also in a form that ensure usability and actual use by the stakeholders.

16.2 Progress to Date – 25th May 2007

In March we invited James Thomas to visit and evaluate our tools from the perspective of an EPPI reviewer, after some encouraging comments and feedback we have extended the clustering prototype to include his recommendations. From further ongoing discussions we are re-examining our evaluation plan to extend to all software prototype deliverables as well as a more systematic approach to investigate the usefulness of the overall service. A report on this and any recommended changes to the evaluation plan will be available as D2.2 in the next period, this will include the design of a questionnaire to investigate current awareness of text mining in the social science community in order to measure success of future planned dissemination activities.

17. Quality Plan

Timing	Compliance With	QA Method(s)	Evidence of Compliance
Lifetime of project	W3C Web standards	Compliance with NaCTeM Website QA Policy, which requires compliance with XHTML 1.0 Transitional and CSS 2	Automated tests are run daily to ensure compliance
Lifetime of project	Fitness for purpose	NaCTeM Software Development Process requires development of unit tests, integration tests, load tests. Integration of tools with the Software Infrastructure will be tested with the Software Infrastructure Compatibility Test Suite.	Software passes automated tests
Lifetime of project	Best practice for software development	Compliance with NaCTeM Software Development Process	Production and validation of documentation, test plans (unit, module, system, regression), profiling, mini-milestones. Technical training as required.
Lifetime of project	Adherence to specifications	NaCTeM Software Development Process requires development of automated acceptance tests to validate that implementations conform to user requirements	Implementations pass automated acceptance tests.
Lifetime of project	Web service standards	Compliance with appropriate W3C Web Services standards	Automated testing
Lifetime of	Accessibility standards	Compliance with NaCTeM Website QA Policy, which	Automated testing

project		requires compliance with W3C Web Content Accessibility Guidelines 1.0 with a conformance level of Triple-A. Compliance with NaCTeM Software Accessibility QA Policy.	
Lifetime of project	Documentation	Compliance with NaCTeM Software Development Process, which requires full documentation of software APIs	Automated checking of documentation during daily build. Regular code reviews.

17.1 Progress to Date – 21st February 2007

Checking for standards compliance is performed automatically for software components, this process is also monitored manually at regular intervals. As the code being customised for the document clustering tool belongs to NaCTeM we ensure that all standards and quality assurance of the previous developments are also implemented to ensure suitability of all changes across the full suite of software. The project web site and project documentation run through a similar procedure with best practice carried out in terms of preservation and maintainability.

Targets for the next period include a review of quality plan in light of any technical changes to the project to assure quality and best practice throughout the process, as well as continued adherence to the standards given in the quality plan.

17.2 Progress to Date – 25th May 2007

No changes have been made to the QA plan and work has continued with these factors in mind. One additional benefit of moving from Cheshire3 to Lucene for the information retrieval component is consistent internal core documentation by the developers. This will make future maintenance and adaptation much easier for external users. This is further enhanced by a full set of unit tests for core Lucene code so any changes made during this project already has benchmarks to measure against for compatibility with other solutions in the community.

18. Dissemination Plan

Timing	Dissemination Activity	Audience	Purpose	Key Message
M3 onwards	Incorporation of project information into NaCTeM web site	Social science community	Awareness, Information, Involvement	Roadmap for availability of summarisation service Support for community call
Lifetime of project	Conference presentations and posters	Peer community User community Funding community	Inform Promote Engage	R & D promulgation Education Technical engagement
End of project	Workshop on text mining in social sciences	User community Peer community	Inform Disseminate Promote	Awareness raising

18.1 Progress to Date – 21st February 2007

Part of the dissemination plan was the construction of a project web site. This has been achieved and integrated into the main NaCTeM site. Over the next period we will add an RSS feed to deliver regular updates and progress on the project as well as any announcements and significant developments. To

ensure dissemination of this source of information we will endeavour to advertise them in suitable locations to promote the work of the project and act a central resource for the growing community.

18.2 Progress to Date – 25th May 2007

In order to maximise the potential for communication with the wider social science community we have worked outside of our current dissemination plan to meet face to face with local research groups to identify the major challenges and potential use-cases. We feel this is vital for ensuring appropriate communication with potential stakeholders in the rest of the UK and ease in the barriers that have traditionally faced similar activities. Instead of demonstrating the tool as a new technology coming from the sciences, it will be more appropriate to show that it has arisen from the needs of the social scientist through clear examples and use-cases. In addition to this we will be targeting general and subject specific social science conferences alongside e-Social Science events in order to approach members of the community who would generally shy away from such areas. Over the next period we will identify key conferences in these areas and submit relevant papers.

We have also been participating in other events during this period including the E-Social Science showcase (28th March), the E-Science showcase (1st May), an industrial presentation at Text Analytics (25 April 2007) and a presentation at Cambridge (2nd May). We have also submitted a paper to the All Hands Meeting in September, but we have yet to hear if this has been accepted. We have discussed dissemination issues with EPPI and expect to hear from them soon about further activities within their own community.

19. Exit and Sustainability Plans

Project Outputs	Action for Take-up & Embedding	Action for Exit
Software Service	Ensure tool address users' needs. Ensure tool is stable and easy to use Ensure availability from web site. Promote use through dissemination activities.	Been involved with community from initial stage of project Ensure source code is well documented. Investigate commercial exploitation and/or open source licensing (via OSS Watch) Long-term service provision.
Software Support	Ensure availability from web site. Provide documentation Integration with NaCTeM help desk	Long term service provision
Community Call Support	Promote through dissemination activities and engagement with user groups Help to build a community of social science text miners via community call project support	Engage with further projects with community as appropriate Continuation within long-term service provision. Pursue integration of community call project outputs in overall NaCTeM service offering (involve OSS watch)

Project Outputs	Why Sustainable	Scenarios for Taking Forward	Issues to Address
Software	Based on proven and state-of-the-art	Partnering with commercial suppliers	Focus on users' requirements

	<p>research</p> <p>Address real needs of users</p> <p>Generic tools which can be applied to different problems.</p>	<p>Provision of commercial hosted services in different domains</p>	<p>IPR and licensing arrangements.</p> <p>Academic versus commercial usage.</p>
--	---	---	---

19.1 Progress to Date – 21st February 2007

During this period we have secured a pilot project with the BBC looking at similar techniques within news feeds. If this high visibility project is successful it may be possible to gain further investment from the BBC and similar organisations to ensure sustainability. Due to its nature, it will also ensure improved dissemination activities and another instance of text mining for general text, making it easier to draw in potential community members from the social sciences. Good progress is being made with the plan, with some outcomes being achieved well in advance of schedule. Our targets for the future months include continuation of work against the plan in order to promote as many possible avenues of sustainability and promotion as possible, whilst maintaining high standards of documentation to ensure preservation options are available.

19.2 Progress to Date – 25th May 2007

Whilst software service issues have been addressed in the previous two sections we need to focus further on software support both in terms of making the tools available on the website and providing access to documentation, both on user and developer levels. These issues are currently being addressed with a web demonstrator of the clustering tools planned for delivery by the end of July. This will include this documentation and relevant FAQ sections to assist in demonstration of the functionality and scope of the tool and the project.

From some of the initial feedback from demonstration audiences and from the community there appears to be a potential for two communities, one from social science users wishing to integrate text mining workflows into their own research and one from resource owners looking to provide additional functionality that would be of use to social scientists. It is unclear at this stage the true numbers involved in these communities or whether it would be useful to merge them. As the call progresses and dissemination activity continues we hope to gain a clearer view of these communities and plan accordingly.

Appendixes

Appendix A. Project Budget

	2005/06 AY	2006/07 AY	2007/08 AY	Total
Staff salary ⁴	£3,107	£38,773	£36,964	£78,844
Overhead ⁵	£4,472	£53,894	£49,618	£107,984
Contribution from University of Manchester ⁶	-£3,014	-£36,394	-£33,576	-£72,984
Dissemination	£1,800	£6,800	£6,800	£15,400
Equipment	£8,856			£8,856
Community call		£161,000	£200,900	£361,900
Total	£15,221	£224,073	£260,706	£500,000

⁴ Assumes pay award of 4% per annum and includes overheads.

⁵ Overhead includes contribution from JISC for estate costs, indirect costs and PI as calculated using the TRAC method, as supplied by John Keane, University of Manchester.

⁶ There is a strong level of commitment from Manchester University to recruit an additional text mining expert as they feel that this resource is vital to the continued growth of NaCTeM. They are therefore prepared to make a significant contribution to the overheads for this person.



WORKPACKAGES	Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
1: Project Management		█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█
2: Requirements and Evaluation				█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█
3: Document Clustering				█	█	█	█	█	█																
4: Information Extraction							█	█	█	█	█	█	█												
5: Summarisation										█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█
6: Service Exemplar																█	█	█	█	█	█	█	█	█	█
7: Dissemination				█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█
8: Support Com. Call									█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█

Project start date: 01-12-2006

Project completion date: 30-11-2008

Duration: 24 months

Workpackage and activity	Earliest start date	Latest completion date	Outputs	Milestone	Responsibility
WORKPACKAGE 1: Project Management Objective: To co-ordinate and manage the work and day-to-day progress. To provide a communication medium between the centre and the funders. Consolidation of the project planning, control, progress and reports, milestone reports, financial statements and budgetary overviews. Coordination with international partners and associated entities.	01/12/06	30/11/08			UoM
T1.1 Project Plan		31/05/06	D1/1 Project Plan		SA
T1.2 Final report: Report on the project's achievements, findings, outcomes, and messages to the JISC community.	01/10/08	30/11/08	D1/2 Final Report		SA
WORKPACKAGE 2: Requirements Gathering and Evaluation Objective: Test data gathering, requirements analysis by users, set up of evaluation methodology, creation of gold standard	01/12/06	30/11/08			EPPI / UoM
T2.1 Gathering test data for analysis	01/12/06	31/03/06	D2/1 Test Data		EPPI
T2.2 Setting up evaluation framework	01/03/07	31/07/07	D2/2 Report		UoM
T2.3 Creation of gold standard	01/04/07	31/07/07	D2/3 Gold Standard		EPPI
T2.4 Final Report on evaluation	01/09/08	31/10/08	D2/4 Final Report on Evaluation		UoM
WORKPACKAGE 3: Document Clustering Objective: Use of document clustering software and integration into the NaCTeM pipeline	01/02/07	31/07/07			
T3.1 Customisation of document clustering software	01/02/07	30/04/07	D3/1 Customised Tool		UoM
T3.2 Integration of document clustering software into pipeline	01/05/07	31/07/07	D3/2 Prototype Clustering Demonstrator	M1	UoM

Workpackage and activity	Earliest start date	Latest completion date	Outputs	Milestone	Responsibility
WORKPACKAGE 4: Information Extraction Objective: Customisation of existing text mining tools for social science applications	01/05/07	31/12/07			UoM
T4.1 Adaptation of named entity recogniser	01/05/07	30/06/07	D4/1 Customised NER tool		UoM
T4.2 Adaptation of chunker	01/07/07	31/08/07	D4/2 Customised chunking tool		UoM
T4.3 Adaptation of shallow parser	01/09/07	31/10/07	D4/3 Customised shallow parser tool		UoM
T4.4 Prototype Information Extraction Demonstrator	01/11/07	31/01/08	D4/4 Prototype IE Demonstrator	M2	UoM
WORKPACKAGE 5: Summarisation Objective: Development of a scalable summarisation engine; integration into existing NaCTeM software infrastructure	01/09/07	31/07/08			UoM
T5.1 Development of 1st prototype summarisation engine	01/09/07	30/01/08	D5/1 Version 1 of summarisation engine	M3	UoM
T5.2 Scaling up engine and evaluation	01/02/08	30/04/08	D5/2 Version 2 of summarisation engine		UoM
T5.3 Integration of summarisation engine into text mining pipeline	01/05/08	31/07/08	D5/3 Version 3 of summarisation engine		UoM
WORKPACKAGE 6: Service Exemplar Objective: Development of service exemplar which demonstrates the full capabilities of the summarisation tool.	01/03/08	30/11/08			
T6.1 Development of service prototype which demonstrates the full capabilities of the summarisation tool	01/12/07	31/08/08	D6/1 Prototype Service	M4	UoM
T6.2 Service Exemplar for Summarisation tool using requirements analysis	01/09/08	30/11/08	D6/2 Service Exemplar		UoM

Workpackage and activity	Earliest start date	Latest completion date	Outputs	Milestone	Responsibility
WORKPACKAGE 7: Dissemination Objective: Development of a Roadmap for availability of summarisation service, presenting work to conferences, organisation of a workshop	01/12/06	31/10/08			
T7.1 Integrate the project into the NaCTeM web site	01/12/06	28/02/07	D7/1 project web site		UoM
T7.2 Organise workshop	01/08/08	31/10/08	D7/2 workshop		UoM
WORKPACKAGE 8: Support for the Community Call Objective: Promote text mining through dissemination activities and engagement with user groups	01/08/07	Ongoing			UoM
T8.1 Community call for text mining in Social Sciences	01/08/07	30/11/07	D8/1 Prepare community call		UoM
T8.2 Engage with Community	01/12/07	30/11/08	D8/2 Prepare joint proposals		UoM

Members of Project Team:
University of Manchester UoM
SA: Sophia Ananiadou
